



Project Vanguard Report

November 2023

This material has been produced by Velonetic for the London insurance market as part of the Blueprint Two programme.



LLOYD'S

Progress

Achieved in last month

1. 2 project managers have joined the team; with a further recruited to join in January completing the team
2. 22 participants have signed contracts, and 9 have filled in onboarding forms
3. Acceleration of engagement as new PMs drive introductory and test plan workshops
4. Hosted multiple participant visits to Velonetic's G4 model office
5. Vanguard environment update delivered and available for connectivity and sequence 2 testing, Group 1 participants onboarded
6. Progressed process maps for PI 10 & 11, including transversal services (e.g., notifications).
7. Business scenario identification for Vanguard testing is in progress
8. Sample of participant EDIs collected and provided to development teams

Current activity

1. Progressing on Contract and Onboarding Forms completion aiming for 100% completion by 15th December
2. Group 1 connectivity and Sequence 2 testing started, planning Group 2
3. Finalising premium processing L4 diagrams (PI 1-11) December and Claims in January 2024
4. Finalising risk, settlement & other processing L4 diagrams (PI 1-11) January 2024
5. Finalising commercials on test tool (Zephyr)
6. QAs working with BAs to develop test scenarios in line with process mapping activity
7. Training development milestones being identified in line with business scenarios and roadmap for testing
8. Liaison with ASG/DXC on new LM Phase 1 Onboarding Form
9. Assessment of 2024 roadmap due to environment delay, PI11 content and revised Build Plan
10. Review participant grouping with a view to realigning into 4 groups (previously 6)


Risks and issues

1. Contract signing and onboarding responses slower than anticipated
2. Build dependencies and test environment readiness
3. December change freezes and holiday periods
4. Tight lead times for ASG EDI issue resolution for January testing

End-to-end Vanguard roadmap (at 30 Nov 23)

2023

2024

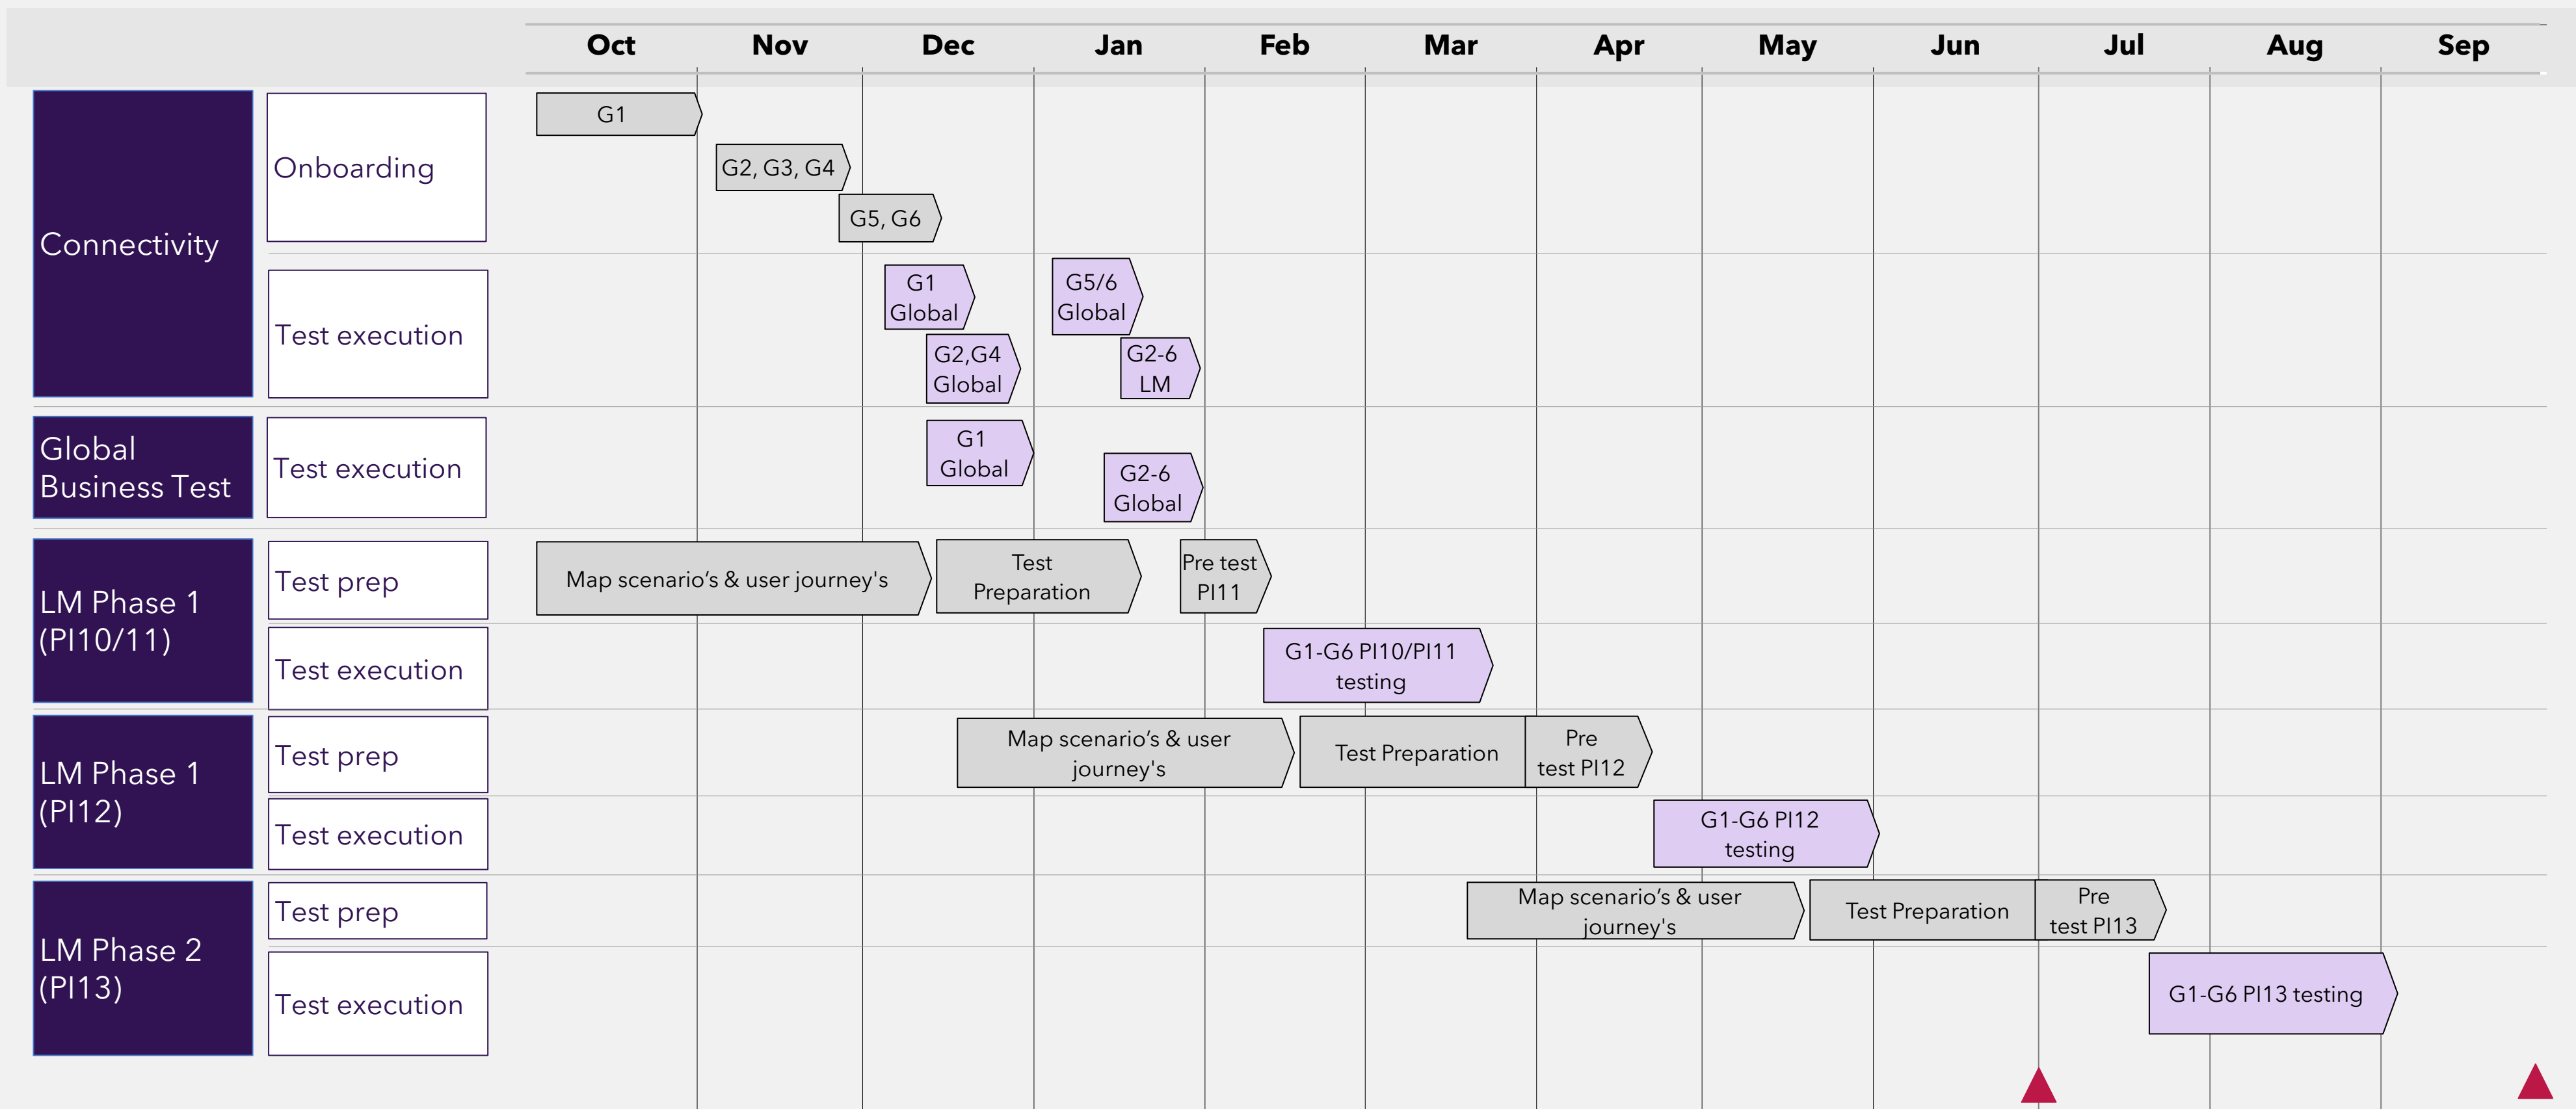

Go live phase 1

Go live phase 2



Velonetic™ is the trading name for Ins-sure Holdings Limited and Xchanging Claims Services Limited. In the following, Velonetic is referred to us as “we”, “us” or “our”. The term ‘you’ or ‘your’ refers to the person or entity using, accessing or viewing this material (defined as “Resources”).

Copyright

Unless otherwise stated, the copyright and any other rights in the contents of the Resources, including but not limited to images, text and data, are owned by us or our licensors.

We will endeavour to acknowledge third-party copyright. If third-party copyright has not been properly acknowledged, please notify us at the address below so that we can make the appropriate arrangements.

You may (unless otherwise specifically stated) download, display or print the Resources for personal use or internal use within an individual organisation for non-commercial purposes.

Please email velonetic@dxc.com with any requests for further authorisation regarding proposed use of the Resources.

We typically grant permission for non-commercial re-use of the Resources, particularly in an academic or education context.

Where we grant permission for re-use of the Resources, we do not accept any responsibility for any alteration or manipulation of the Resources.

Where we grant permission to translate Resources, we do not warrant that we have reviewed or will review the translation for accuracy or completeness.

Where Resources include or are comprised of third-party copyright materials, the copyright of that material remains with the originating individual or organisation and any re-use is subject to the separate approval of the relevant third party.

If you have a complaint about how your application has been handled or you would like a review of the decision made in relation to your application, please write to the above address or email to velonetic@dxc.com.

[Velonetic's Terms & Conditions](#)
